

Work Order ID 139012

Friday, November 20, 2015 1:45:42 PM

139012

Page 1

Item ID: D4149-1 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Crosstube Lug Plate, Aft
 Start Date: 11/13/2015 Start Qty: 28.00 ***28*** Cust Item ID:
 Required Date: 11/13/2015 Req'd Qty: 28.00 ***28*** Customer:
 Reference:

Approvals: Process Plan: MCS Date: **NOV 20 2015** Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D4149	C

100 0.00

100

Waterjet
FLOW CNC Waterjet

Memo

Cut as per dwg D4149
 Prog Rev: C
 Dwg Rev: C

OPEN TO HOLES TO FINISH SIZE AS PER DWG

Deburr as required

110 0.00

110

QC
Quality Control

Memo

QC2- Inspect parts off machine FAI/FAIB

0.00

(28) _____ 16/01/06

(28) _____ 16/01/06

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : ☐					

Work Order ID 139012

Friday, November 20, 2015 1:45:42 PM

139012

Page 2

Item ID: D4149-1 Accept ***N900040100*** Setup Start ***NS1***
 Revision ID: Stop ***NS2***
 Item Name: Crosstube Lug Plate, Aft
 Start Date: 11/13/2015 Start Qty: 28.00 ***28*** Cust Item ID:
 Required Date: 11/13/2015 Req'd Qty: 28.00 ***28*** Customer:
 Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____ Run Start ***NR1***
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC8- Inspect parts - second check	0.00							
120									
QC	Memo	0.01							
Quality Control									
150	Identify as per dwg & Stock Location: 57086	0.00							
150									
Packaging	Memo	0.00							
Packaging									
160	QC21- Final Inspection - Work Order Release	0.00							
160									
QC	Memo	0.05							
Quality Control									

20160111

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐	☐	No Re-verification ☐	☐	Pressure/Forced ☐	☐	Temperature/Cure ☐	☐
Design ☐	☐	Operator ☐	☐	Bending ☐	☐	Set-up ☐	☐
Doc/Data ☐	☐	Offset/Setup ☐	☐	Centre Not Concentric ☐	☐	BOM/Route ☐	☐
Equip/Tooling ☐	☐	Supplier ☐	☐	Cracks ☐	☐	Broken/Damage/Defect ☐	☐
Handling/Pre ☐	☐	Training ☐	☐	Crimp/Kink/Ripple/Wave ☐	☐	Inspection Incomplete/Unqualified ☐	☐
Material ☐	☐	Use for Testing ☐	☐	Cuffs ☐	☐	Contamination ☐	☐
Internal Transport ☐	☐	Poor Information ☐	☐	Crushing ☐	☐	Countersink ☐	☐
Tribal Knowledge ☐	☐	Rushing ☐	☐	Heat Treat ☐	☐	Cut Too Short ☐	☐
LOA ☐	☐	Product Improvement ☐	☐	Wave/Twist in Tube ☐	☐	Instructions Incomplete/Unclear ☐	☐
Substation ☐	☐	Process Improvement ☐	☐	Marks/Chatter ☐	☐	Drill Holes ☐	☐
Past Expiry Date ☐	☐	Manufacturing Process ☐	☐	OTHER : _____			
Misidentified ☐	☐	Past Due ☐	☐				

Picklist Print

Friday, November 20, 2015 1:45:45 PM

Page 1

Work Order ID: 139012

139012

Parent Item: D4149-1

D4149-1

Parent Item Name: Crosstube Lug Plate, Aft

Start Date: 11/13/2015

Required Date: 11/13/2015

Start Qty: 28.00

Required Qty: 28.00

Comments: IPP Rev:A 10.06.24 new issue DD verf:EC
IPP Rev:B 11.03.03 as per revC DD verf:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304S11GA		Purchased		No		100	sf	121.2750	0.1355	3.993685			

M304S11GA

304/316 0.125 Sheet

**

DL 16/01/07

Location

Loc Qty

Loc Code

MAT020

121.27498

M128254

34.975

M129545

30.24998

M129972

56.05

5.3

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :							
Misidentified	☐	Past Due	☐								

DART AEROSPACE LTD		Work Order: 139012
Description: Aft Crosstube Lug Plate		Part Number: D4149-1
Inspection Dwg: D4149	Rev: C	Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST


Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
Ø0.129	+0.005/-0.001	Ø.129	/		Vid-02	
Ø0.191	+0.005/-0.001	Ø.192	/		Tape	
Ø0.257	+0.006/-0.001	Ø.258	/			
Ø0.38	+0.006/-0.001	Ø.379	/			
0.380	+/-0.010	.386	/			
0.469	+/-0.010	.469	/			
0.310	+/-0.010	.314	/			
0.750	+/-0.010	.758	/			
3.25	+/-0.030	3.25	/			
0.65	+/-0.030	.65	/			
0.63	+/-0.030	.63	/			
5.46	+/-0.030	5.46	/			
3.80	+/-0.030	3.80	/			
2.13	+/-0.030	2.13	/			
1.313	+/-0.010	1.307	/			
0.625	+/-0.010	.623	/			
0.375	+/-0.010	.374	/			
1.175	+/-0.010	1.178	/			
0.752	+/-0.010	.750	/			
1.588	+/-0.010	1.583	/			
1.587	+/-0.010	1.584	/			
11.15	+/-0.030	11.15	/			
0.750	+/-0.010	.740	/			
1.55	+/-0.030	1.50	/			
1.12	+/-0.030	1.12	/			
8.42	+/-0.030	8.42	/			
2.70	+/-0.030	2.70	/			
0.125	+/-0.010	.116	/			
Ø0.252	+0.003/-0.000	Ø.253	/			

Measured by: ac
Date: 16/01/11

Audited by: PD
Date: 16-01-12

Preliminary Approval:
Date:

Rev	Date	Change	Revised by	Approved
A	10.08.04	New Issue	KJ	
B	12.02.01	Dimensions updated per Dwg Rev C	KJ	

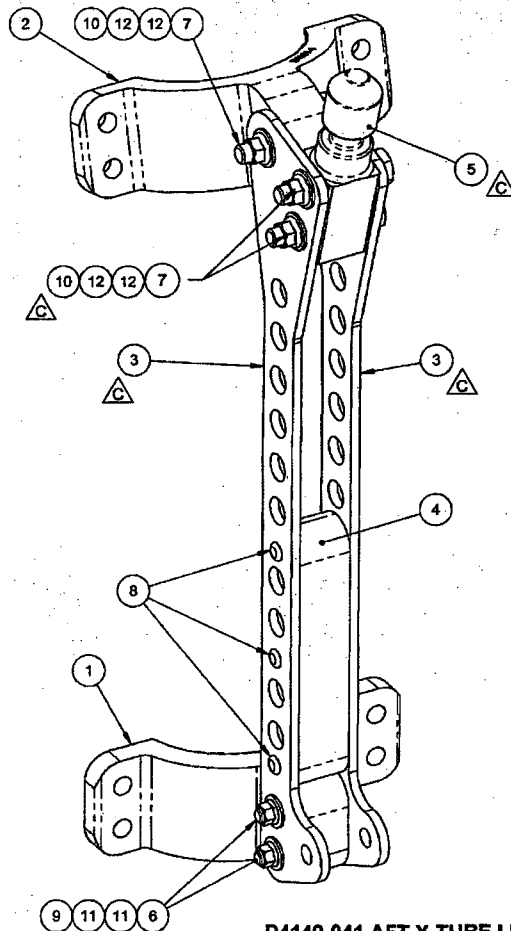

D4149-041 AFT X-TUBE LUG ASSY

NOTES:



- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4149-041" USING FINE POINT PERMANENT INK MARKER
- 7) WEIGHT: 2.21 lbs

ITEM	QTY	P/N	DESCRIPTION
	X	D4149-041	AFT X-TUBE LUG ASSY
1	1	D3910-1	X-TUBE LUG
2	1	D4091-1	MOUNTING LUG
3	2	D4149-1	AFT X-TUBE LUG PLATE
4	1	D4149-3	SPACER
5	1	D4149-5	EYEBOLT STUD
6	2	AN3C12A	BOLT
7	3	AN4C13A	BOLT
8	3	MS20815-4M18	RIVET
9	2	MS21043C3	NUT
10	3	MS21043C4	NUT
11	4	NAS1149C0332R	WASHER
12	6	NAS1149C0432R	WASHER

COPY
 TO
 FROM
 COPY
 COMMENT
 DATE
 139012 MJS
 15-11-17
 RELEASED
 2011-02-24
 JWP

C	HOLE DIA CHANGED TO 0.252" (D8-3); HOLE DIA CHANGED TO 0.250" (C8-5); REPLACED QTY(2) AN3C12A, MS21043C3 AND QTY(4) NAS1149C0332R WITH QTY(2) AN4C13A, MS21043C4 AND QTY(4) NAS1149C0432R (D3-1, D7-2)	SC	11.02.22
B	MS20815-4M18 WAS MS20815-4M20 (ZN D3-1 & B7-2); ADDED D4149-5 (SHT 5); D4149-5 WAS D3909-5 (ZN D3-1 & D7-2); REPLACED QTY(3) MS20815-4M18 WITH QTY(2) EACH AN3C12A, MS21043-3 AND QTY(4) NAS1149C0332R WASHER (ZN D3-1, C7-1, B7-2 & B3-2); Ø.191 2 PL REPLACES Ø.129 3 PL (ZN D8-3); REASON: SEE TR-D350-807-2 REV. B.	MB	10.07.05
A	NEW ISSUE	MB	10.06.18
REV.	DESCRIPTION	BY	DATE
DESIGN	MB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	SC		
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 1 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

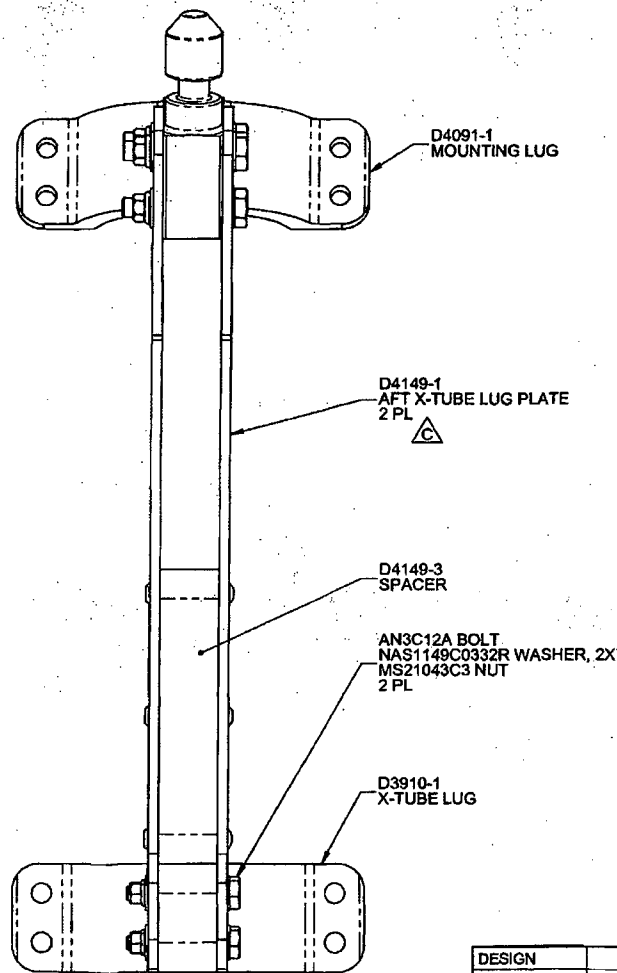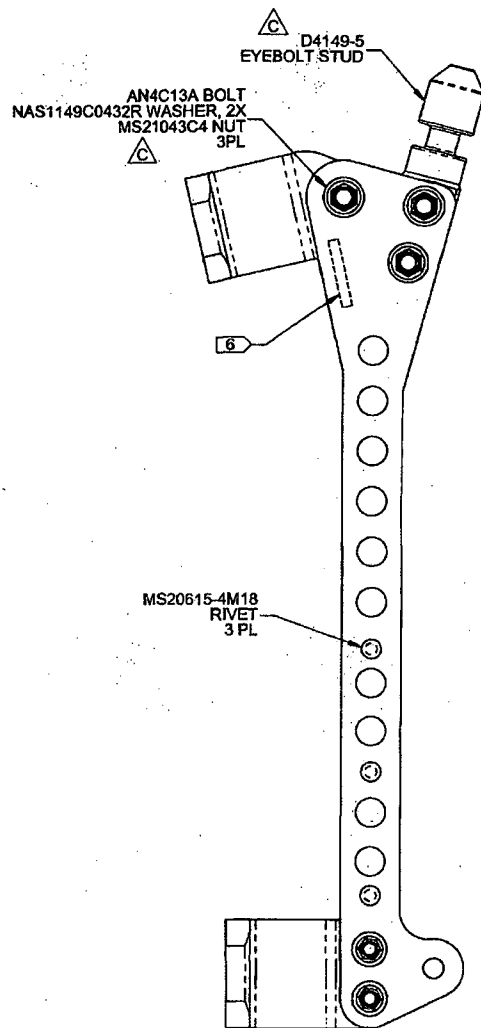


D4149-041 AFT X-TUBE LUG ASSY

RELEASED
2011-02-24
MP

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 2 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL. USE IS LIMITED TO THE EXPIRED CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	



8 7 6 5 4 3 2 1

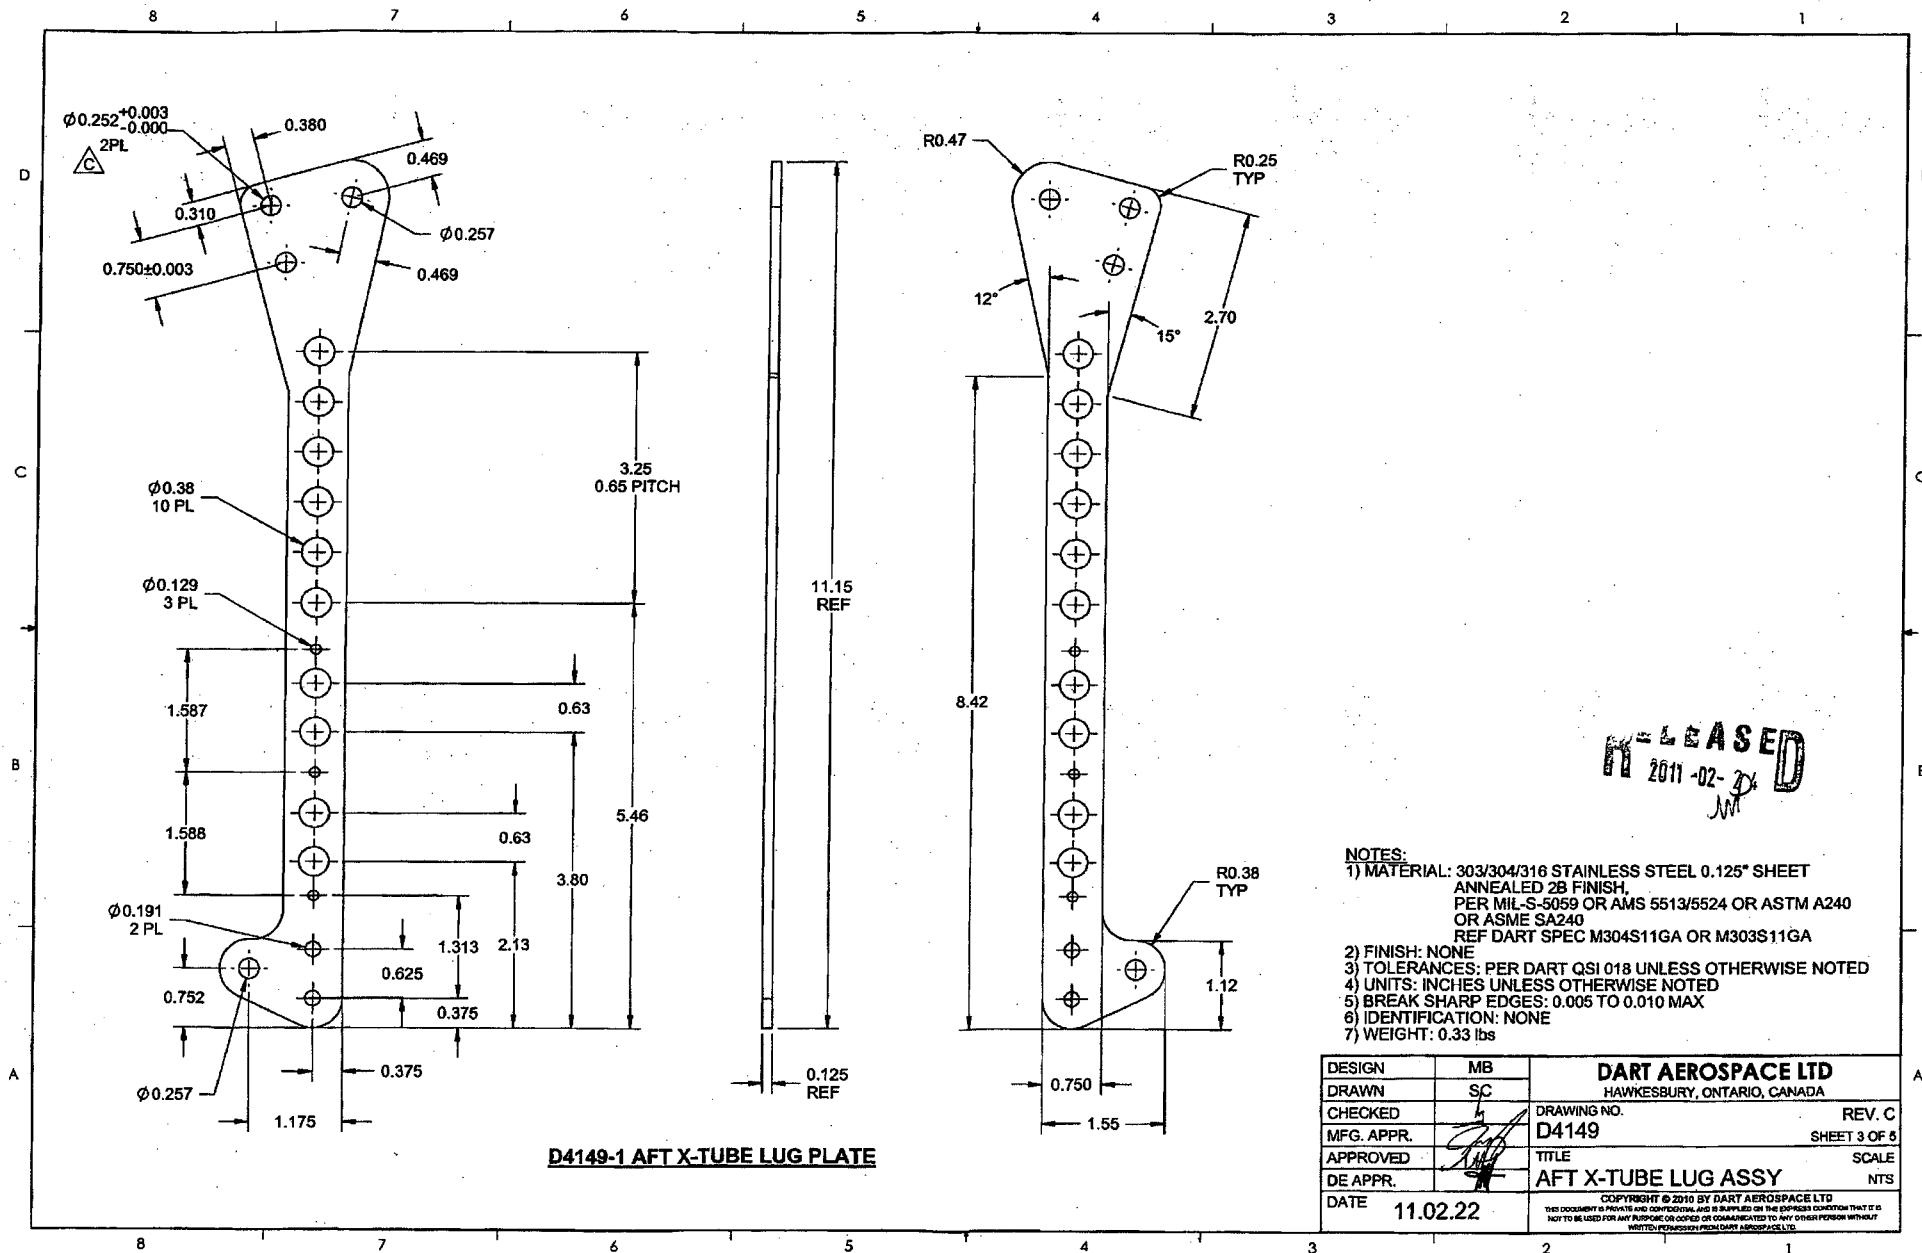


RELEASED
2011-02-24

- NOTES:**
- 1) MATERIAL: 303/304/316 STAINLESS STEEL 0.125" SHEET
ANNEALED 2B FINISH
PER MIL-S-5059 OR AMS 5513/5524 OR ASTM A240
OR ASME SA240
REF DART SPEC M304S11GA OR M303S11GA
 - 2) FINISH: NONE
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: NONE
 - 7) WEIGHT: 0.33 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 3 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS UNDERSTANDING THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

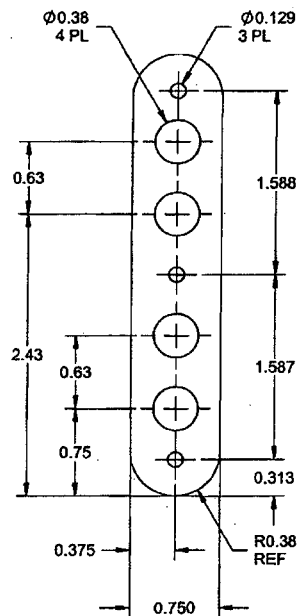

D4149-3 SPACER





RELEASED
2011-02-24

NOTES:

- 1) MATERIAL: 303/304/316 STAINLESS STEEL BAR PER ASTM A276 OR A582
REF DART SPEC MS304B OR MS303B
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK ALL SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.47 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 4 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS UNDERSTANDING THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

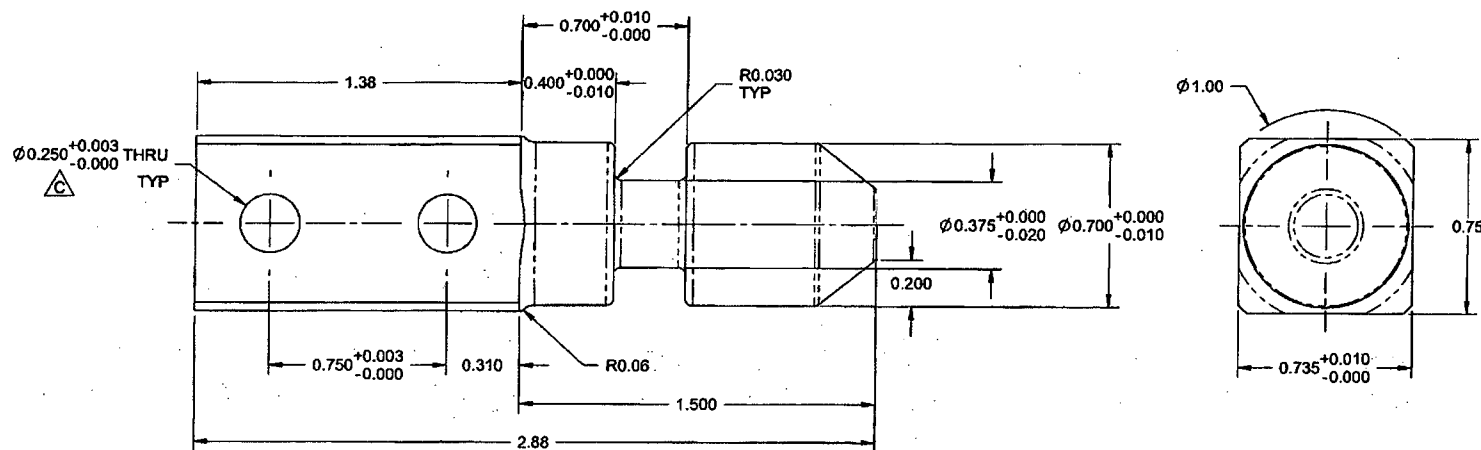

D4149-5 EYEBOLT STUD

RELEASED
2011-02-26

NOTES:

- 1) MATERIAL: 303/304/316 STAINLESS STEEL BAR PER ASTM A276 OR A582
REF DART SPEC MS304B OR MS303B
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK ALL SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4149-5" USING FINE POINT PERMANENT INK MARKER
- 7) WEIGHT: 0.32 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 5 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS UNDERSTANDING THAT IT IS NOT TO BE LOANED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
